





Structure: CIB 24" x 36"
 Job Number:
 Job Name: Jones and Sons Precast
 Job Location:

Specification: 24"x36"
 Contractor:



Based on:
 Take Off By: 2/4/2020 Caleb

Design Build Height Top of Casting + 500.00' Floor Elevation - 496.00' Design Height = 4.00'		Stack Build Height Base Gain + 4.00' Design Height = 4.00' Floor Thickness + 0.67' Outside Height = 4.67'		Manufacture Date:	
				Ship Date:	
				Frame/Ring:	
				Channel:	
				Coating:	
				Mix:	
				Notes: Sizes can vary from 12" to 60"	

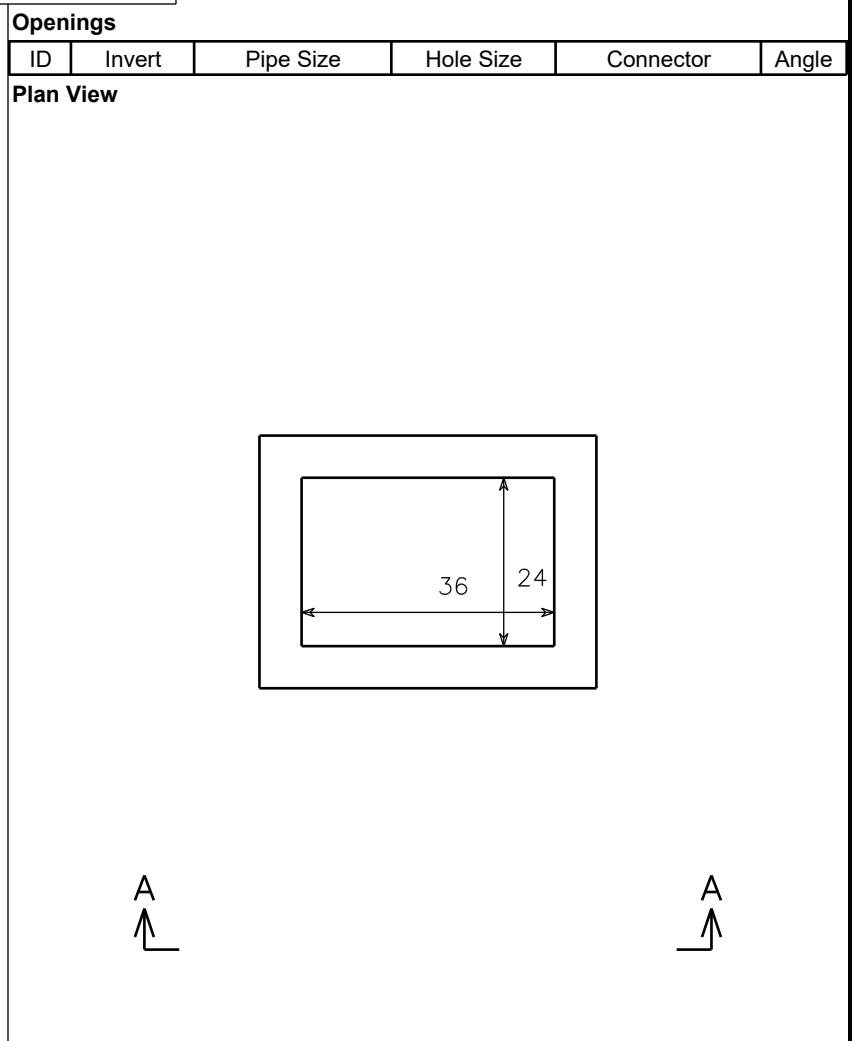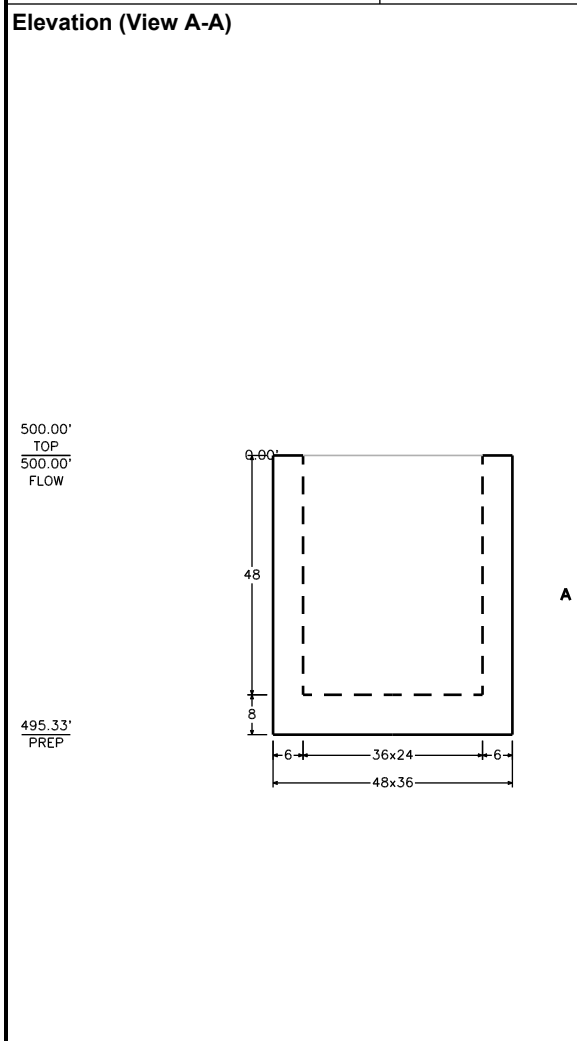

BOM For Stack

ID	Description	Qty.	Weight
A	24"x36" Base 8F 48HI	1	4,789
Totals (precast, lbs)		1	4,789
